

Commonwealth of Virginia
Charlie Kilpatrick, PE,
Chief Deputy Commissioner
Virginia Department of Transportation

Route 58 – Phase 3

Project Briefing


December 7, 2011



Route 58 - Phase 3 Project Summary

- **Execute Comprehensive Agreement** **December 2003**
 - **Branch Highways, Inc**
- **Phase 1 - Notice to Proceed** **December 2003**
 - **Meadows Of Dan Section**
 - **Construction Completed** **June 2005**
- **Phase 2 – Notice To Proceed** **October 2007**
 - **Hillsville Bypass**
 - **Open to Traffic** **August 2011**
- **Phase 3 – Notice to Proceed** **December 2011**
 - **Tri-County & Laurel Fork Sections**

Route 58 – Phase 3 Project Location

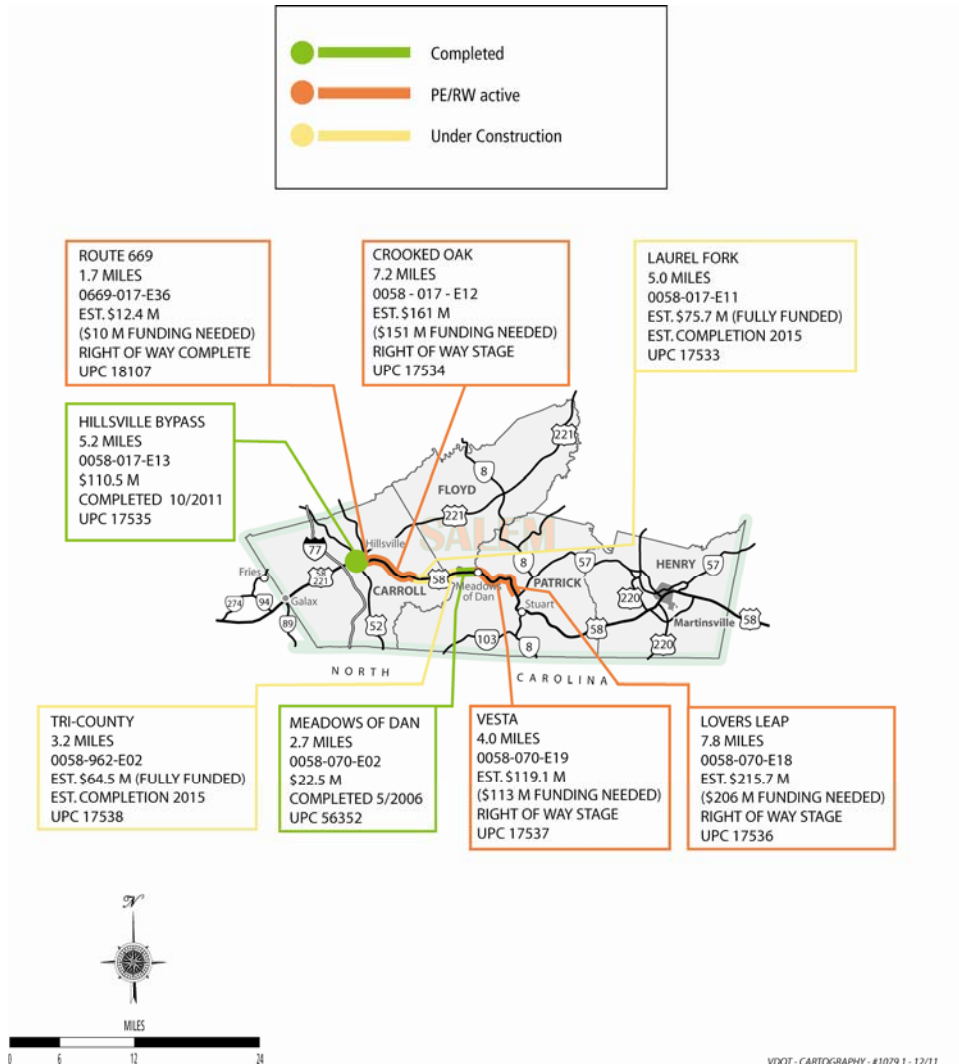

Route 58 - Phase 3 Project Summary

- **Contractor: Branch Highways, Inc**
- **Project Sections**
 - **Tri-County Section – 3.2 Miles**
 - **Laurel Fork – 5.0 miles**
- **Scope of Work –**
 - **Fixed Price, Fixed Date Design-Build Contract**
 - **8.2 Miles of 4-lane Divided Highway**
 - **Permitting & Wetland and Stream Mitigation**
 - **Right of Way Acquisition**

Route 58 - Phase 3 Project Summary

- **Contract Price = \$119,750,000**
- **Project Schedule:**
 - **Notice To Proceed:** **December 15, 2011**
 - **Construction Completion** **December 2015**
